
The PO Board

Planning with the right level of detail at the right time

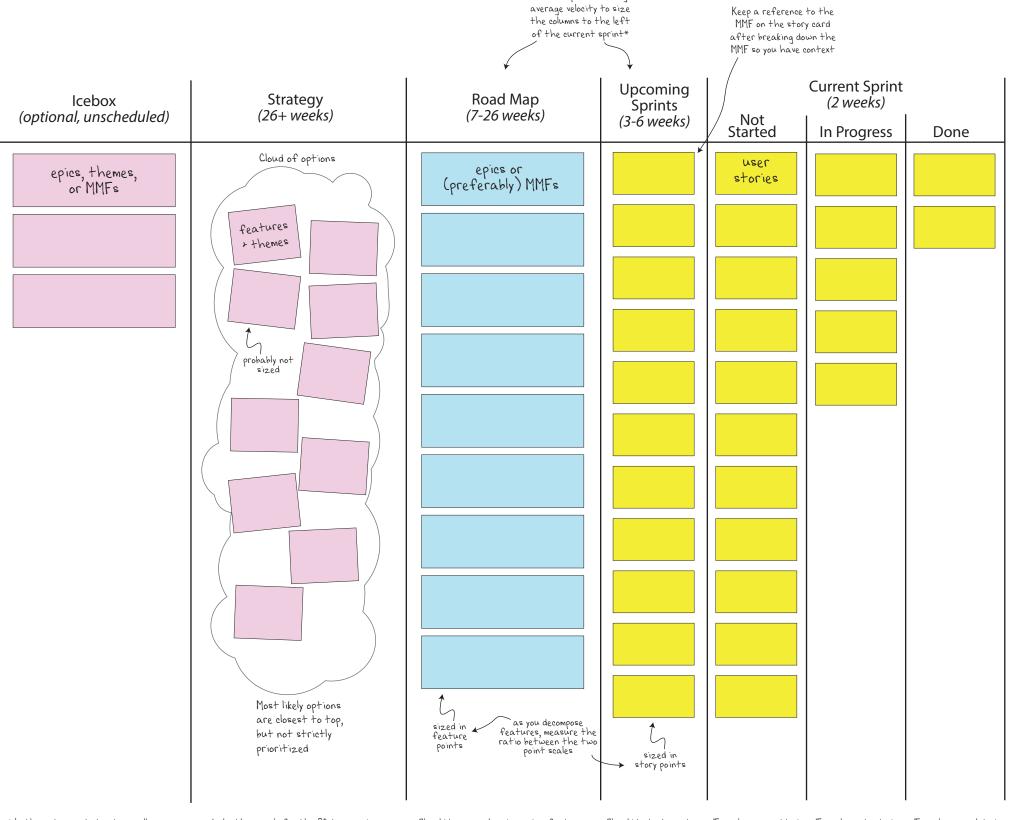

Use a 3 sprint trailing

Some teams extend the board to the right to capture states beyond "done in the current sprint." For example, completed stories might wait in a queue until a whole MMF is complete and then the MMF would move to "Ready to Deploy."

*To make external commitments, consider reducing velocity for columns to the left of the current sprint using these risk factors:

To get this	Divide velocity by	
confidence level	Rigorous	Risky
10%	1	1
50%	1.4	2
90%	1.8	4

To get into this column...

Worth capturing, but not compelling or well-defined enough to plan into the next year or two of work. May function as an "out of scope" or "not in our vision" list.

Valuable enough for the PO to consider over the next I-2 years.

Should be minimal and sized in feature points.

Should be broken into user stories that satisy the INVEST criteria and sized in story points. Team has committed to these stories in the current sprint.
Should be sized so that 6-10 per team

will fit.

Team has completed these stories according to their story definition of done.

